

In-Process QC Checklist for Stationary Kavach Installation

QC Engineer Name: surya

v1.0

Station ID	Station Name	Zone	Division	Section Name	Initial Date	Updated Date
4556	Panvel	CR	Mumbai	Mumbai	2025-09-05	2025-09-05

Total Points	Closed Points	Open Points
106	3	103

Start Date & Time	Completed Date & Time	Total Time
2025-09-05 16:16:03	2025-09-05 16:30:46	0h 14m 43sec


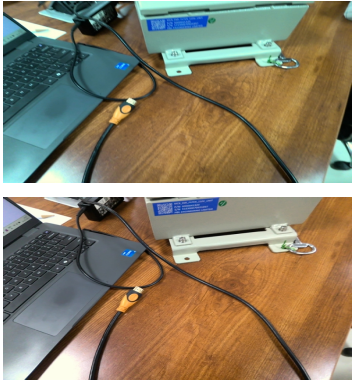
Completion Status	☐ Completed	☒ Not Completed
-------------------	------------------------------------	---

1.0 VERIFICATION OF SERIAL NUMBERS OF EQUIPMENT AS PER IC

S.No	Description	Status	Remarks	Image
1.2	Peripheral Processing Card 1 516138201023094	Matching		
1.3	Peripheral Processing Card 2 516329200952009	Not Matching		
1.7	Voter Card 1	Not Installed		

2.0 Tower and RTU

Start Date & Time	Completed Date & Time	Total Time
5/9/2025, 4:25:19 pm	5/9/2025, 4:25:19 pm	0h 0m 0sec

S.No	Description	Status	Remarks	Image
2.2	Verification of RF Antenna Fixing and LMR Cable Routing: The mounting of all antennas on the tower shall be at the same level, and check whether the antennas are properly fixed with clamps at the bottom side of each antenna.	Fixed		
2.3	Verification of RF Antenna Fixing and LMR Cable Routing: Verify the RF cable joining to antenna and ensure that no cable joints are used from the tower location box to the antennae, and confirm that the patch cords used are of minimum length.	Joined		

3.0 Station TCAS

Start Date & Time	Completed Date & Time	Total Time
5/9/2025, 4:25:33 pm	5/9/2025, 4:25:33 pm	0h 0m 0sec

S.No	Description	Status	Remarks	Image
3.1	Visual Checks: Ensure that the equipment barcode sticker is available, cable entries at Kavach are properly closed with rubber gaskets or grommets, all modules are free of dirt and dust and are neatly fitted into the KAVACH rack as per the installation manual, and that no loose wires are hanging.	Found Ok		
3.2	Verification of equipment placement and cable routing as per Relay Room Layout.	Routing Done		

Note : This QC report is generated by the system and does not need a physical signature.
